


WEEKLY UPDATE

www.lscivil.co.nz

Number #001 – Week Ending 30/07/2023

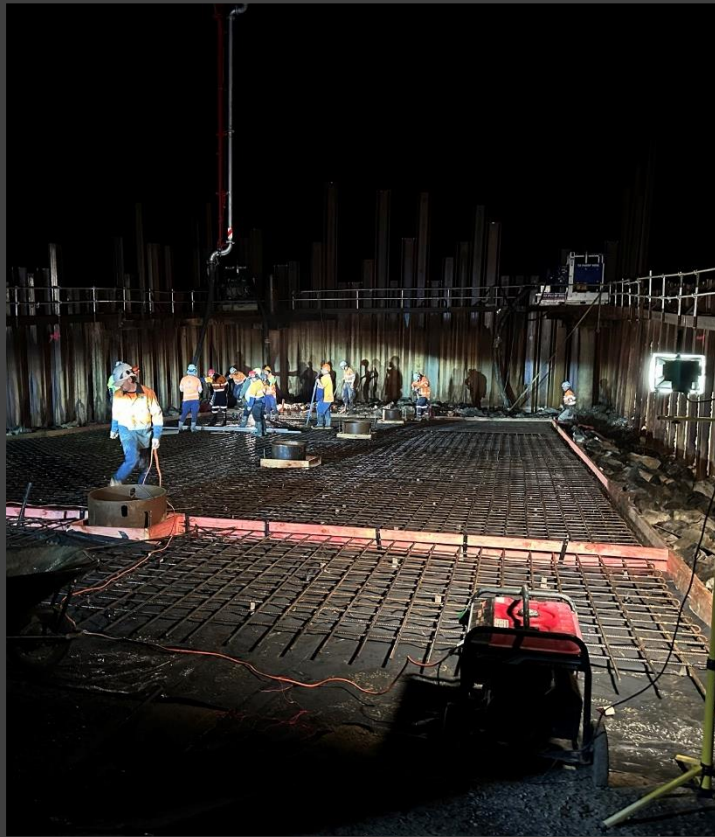

Recreational Boat Ramp

This week on site saw a lot of progress made on the recreational boat ramp. Our team put in some big hours to ensure everything ran smoothly with no delays.

On Monday, prep work for the lower half of the ramp was completed with final height cuts made, installation of reinforcing steel and formwork constructed for concrete, followed by quality inspections.

Tuesday was a big day with the first concrete pour underway at 5:30am, we had a lot of help from Ian Howe Concrete Pumps and Compass Concrete, a big thank you to both of your teams.



Tuesday and Wednesday we did it all again, finalising heights, installing reinforcing steel, constructing formwork, and completing quality inspections.

The weather cleared up Thursday morning and gave us perfect conditions for pouring the rest of the ramp.



What's next?

We will be adding the finishing touches to the recreational boat ramp, sealing off the saw cuts, remedying any defects and placing the last of the rock around the edges of the ramp to set it in place with the rest of the sea wall.

We will then demobilise from the ramp and hand it over to Herons while we continue the sea wall at the Southern end from Ch250m onwards.

Thanks for working with Land + Sea Civil
We hope you have a great weekend.
