

WEEKLY UPDATE

www.lscivil.co.nz


Number #002 – Week Ending 06/08/2023



Recreational Boat Ramp, nearing completion!

On Monday we installed Geocloth over the batter either side of the boat ramp and along the toe. Afterwards we began placing rock along the sides with our Long Reach excavator.


The lower section of the sides and the toe were then completed using our 5.5t excavator with rubber tracks.

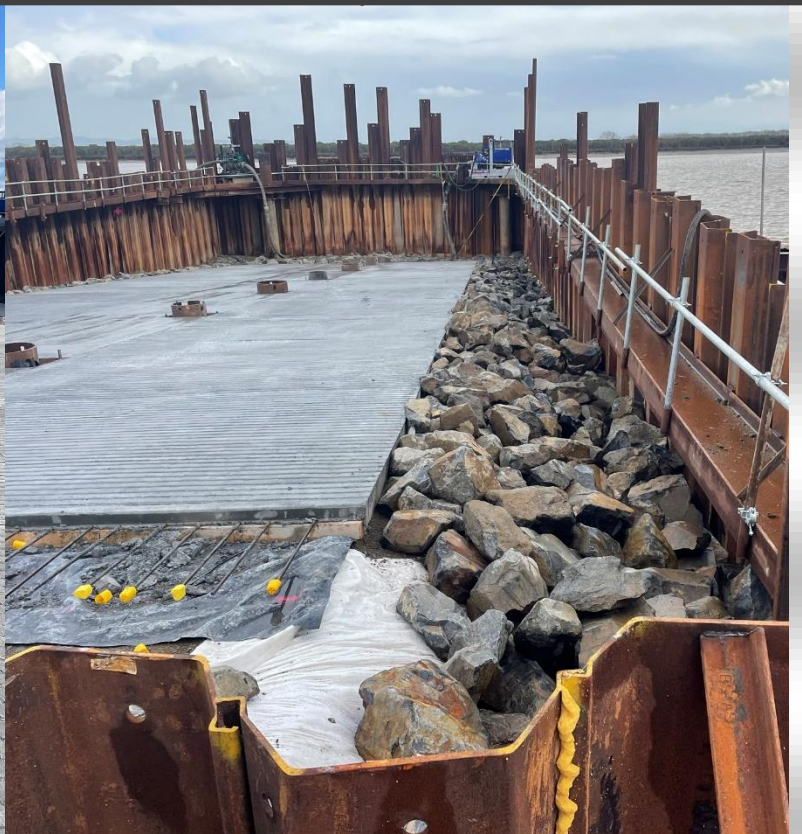

Once the rocks were all in place, we swept the boat ramp and blew out all the saw cuts with a compressor before applying Sika 11FC Sealant to all of the saw cuts.

One final check was made to ensure all rocks were keyed into place and all saw cuts were properly sealed and any defects remedied.

We removed all excess materials away from the ramp area and tidied up our site ready for handover to Herons to begin their works on the recreational boat ramp.

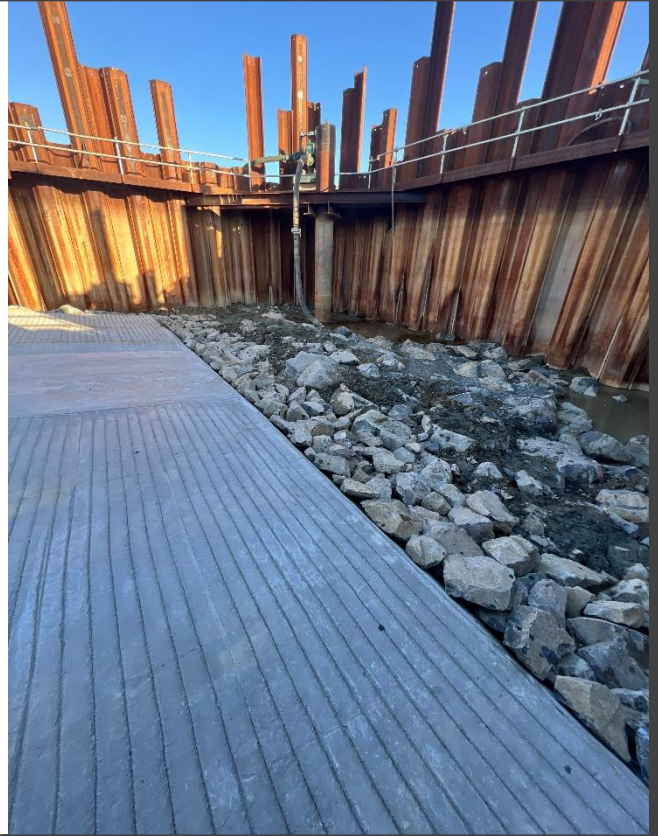

Thanks for working with Land + Sea Civil
We hope you have a great week.
